


PERT CHART

Approved For Release 2003/12/04 : CIA-RDP78B05477A000400040126-9

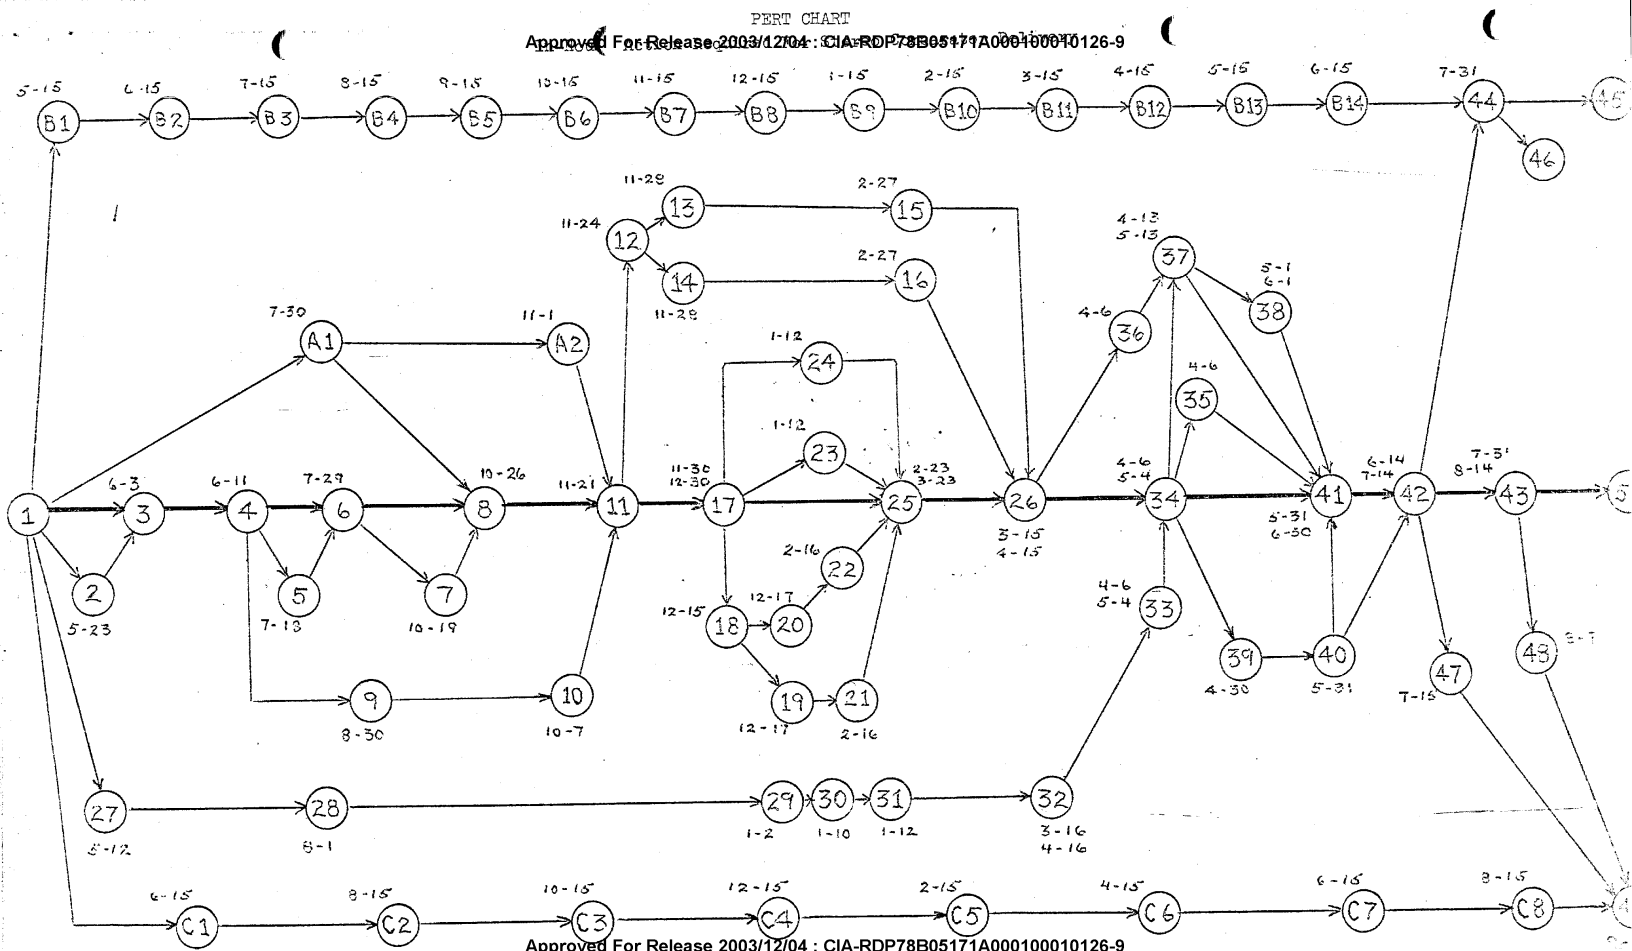

Approved For Release 2003/12/04 : CIA-RDP78B05171A000100010126-9

Declass Review by NIMA/DOD

EVENTDESCRIPTION

	1	Stereo Comparator Fabrication at	25X1
	2	IEG/PHD Provide Coordinate Test Data	
25X1	3	Digital Input Tests at	
25X1	4	Evaluate Digital Test Results Submit Spare Parts List to TSSG/ESD	
	5	IEG/PHD Provide Additional Test Data	
	6	Computer Driven Tests at	25X1
25X1	7	PSG/AID test Data Output for Compatibility	
	8	PSG/AID report results to	25X1
	9	TSSG/ESD review and revise Spare Parts List	
25X1	10	TSSG/ESD contract with for the revised Spare Parts List	
	11	Final Assembly of Subsystem (less optics) by	25X1
25X1	12	submit draft of Operating and Maintenance Manuals to TSSG/DED	
	13	IEG/PHD review and revise Operating Instruction Manual	
	14	TSSG/ESD review and revise Maintenance Manual	
	15	IEG/PHD approve Operating Instruction Manual	
	16	TSSG/ESD approve Maintenance Manual	
25X1	17	start final assembly at	25X1
	18	submit draft of Test Plan to TSSG/DED	
	19	IEG/PHD review Operational Test Plan	
	20	TSSG/ESD review and revise Test Plan	
	21	IEG/PHD approve Operational Test Plan	
	22	TSSG/ESD approve Test Plan	
	23	IEG/PHD provide representative imagery for pre-acceptance test	
	24	TSSG/ESD provide test targets and equipment	25X1
	25	System completely checked out and ready for pre-acceptance test at	
	26	Pre-acceptance test completed	
	27	Final design of Clean Room reviewed and approved by Logistics-Arey	25X1
25X1	28	Site Preparation for Clean Room started	
	29	Clean Room site completed	
25X1	30	Logistics checkout Clean Room	
25X1	31	crew install cable trays, heavy wiring, etc. in Clean Room	25X1
	32	Clean Room and Black Box checkout based on operation of instrument at	
	33	Logistics provide GSA moving crew	
25X1	34	starts installing the instrument in Clean Room	25X1

EVENT	DESCRIPTION
	35 On-the-job Maintenance Training as instrument is installed
25X1	36 ☐ submit draft of Programming Manual to PHD
	37 ☐ train IEG/PHD in instrument operation
	38 IEG/PHD to provide operational imagery for acceptance tests
	39 PSG/AID to have stereo and mono on-line programs ready to go
	40 PSG/AID to make maximum on-line time available 5-31 to 6-19 (6-30 to 7-17 late dates) to checkout and run acceptance tests on the instrument
	41 Installation complete and acceptance tests start
25X1	42 NPIC ☐ acceptance tests complete
	43 Final Acceptance Test by IEG/PHD and TSSG/ESD to be completed by 7-31 (8-14 late date)
25X1	44 ☐ submit final documentation to TSSG/DED
	45 As built drawings completed
25X1	46 ☐ submit all reports, drawings, ray traces, subcontractor reports, etc.
25X1	47 NPIC - Contracts pay ☐ remaining progress payments 7 1/3% on each of following dates: 30, 60, 90 days after installation
	48 Final Report on acceptance tests from IEG/PHD and TSSG/ESD to TSSG/DED
	49 Incentive Fee Awarded and contract completed
	50 Operational Tests and Training by IEG/PHD
	A-1 FY-70 funding provided to complete project
	A-2 Project out of funds if FY-70 funds is not provided
25X1	B1-B14 ☐ submits monthly and technical reports to TSSG/DED. Copies provided to IEG/PHD, TSSG/ESD and Logistics
	C1-C8 TSSG/DED submits contract inspection reports to Contracts Administration

IEG/PHD	TSSG/ESD T&E//Maint.		LOGISTICS	PSG/AID	TSSG/DED	NPIC/PPBS MANAGEMENT
2, 3, 4, -5,	11	4, 9	27, 28, 29, 30,	7, 8, 39,	3, 4, 6, 11,	A-1
6, 13, 15, 19,	20	10	31, 32, 33, 34,	40	12, 18, 25,	A-2
21, 23, 25,	22	14	41, 42, 43		26, 34, 41,	
26, 36, 37, 38,	24	16			42, 43, 44,	
41, 42, 43, 48	25	35			46, 48, 49	
	26	45				
	41					
	42					
	43					
	48					

Approved For Release 2003/12/04 : CIA-RDP78B05171A000100010126-9

UNCLASSIFIED		CONFIDENTIAL		SECRET	
OFFICIAL ROUTING SLIP					
TO	NAME AND ADDRESS	DATE	INITIALS		
1					
2	<i>Barrera - File Continued File</i>				
3					
4					
5					
6					
ACTION		DIRECT REPLY		PREPARE REPLY	
APPROVAL		DISPATCH		RECOMMENDATION	
COMMENT		FILE		RETURN	
CONCURRENCE		INFORMATION		SIGNATURE	
Remarks: <i>Good job - The trick is to make it work, now, I'm sure you can do it -</i> <i>[Signature]</i> "Dave"					
FOLD HERE TO RETURN TO SENDER					
FROM: NAME, ADDRESS AND PHONE NO.					DATE
UNCLASSIFIED		CONFIDENTIAL		SECRET	

Approved For Release 2003/12/04 : CIA-RDP78B05171A000100010126-9

CENTER ROUTING SLIP

FROM			DATE
TSSG/DED			2 June 1969
TO	INITIALS	DATE	REMARKS
DIRECTOR			<u>FYI</u> Good/Hu
DEP/DIRECTOR			
EXEC/DIRECTOR	2	Hu 6/6	
SPECIAL ASST	1	M 6/6	
ASST TO DIR			
ASST TO DEP/DIR			
CH/PPBS			
DEP CH/PPBS			
EO/PPBS			
CH/IEG			
DEP CH/IEG			
EO/IEG			
CH/PSG			
DEP CH/PSG			
EO/PSG			
CH/TSSG	3	JUL 6/1	C/DED - a final piece 1
DEP CH/TSSG			
EO/TSSG			
CH/SSD/TSSG			
PERSONNEL			
LOGISTICS			
TRAINING			
RECORDS MGT			
SECURITY			
FINANCE			
DIR/IAS/DDI			
CH/DIAXX-4			
CH/DIAAP-9			

ILLEGIB
